

# **Update on the Anderson Dam Seismic Retrofit Project, Coyote Creek Flood Protection Project, and Collaborative Encampment Outreach and Cleanup**

**Santa Clara Valley Water District & San José City Council Joint Meeting  
August 19, 2025**

**San José City Hall / Santa Clara Valley Water Headquarters Building**

**Ryan McCarter, P.E. Deputy Operating Officer - Santa Clara Valley Water District  
Olympia Williams, Deputy Director – Parks, Recreation and Neighborhood Services, City of San José**

## **Anderson Dam Seismic Retrofit Project & Coyote Creek Flood Protection Project**





# Anderson Dam Seismic Retrofit Project & Coyote Creek Flood Protection Project




# Anderson Dam Seismic Retrofit Project

Unlined Spillway

Extension of concrete over currently unlined channel

Coyote Creek  
North Channel

South Channel

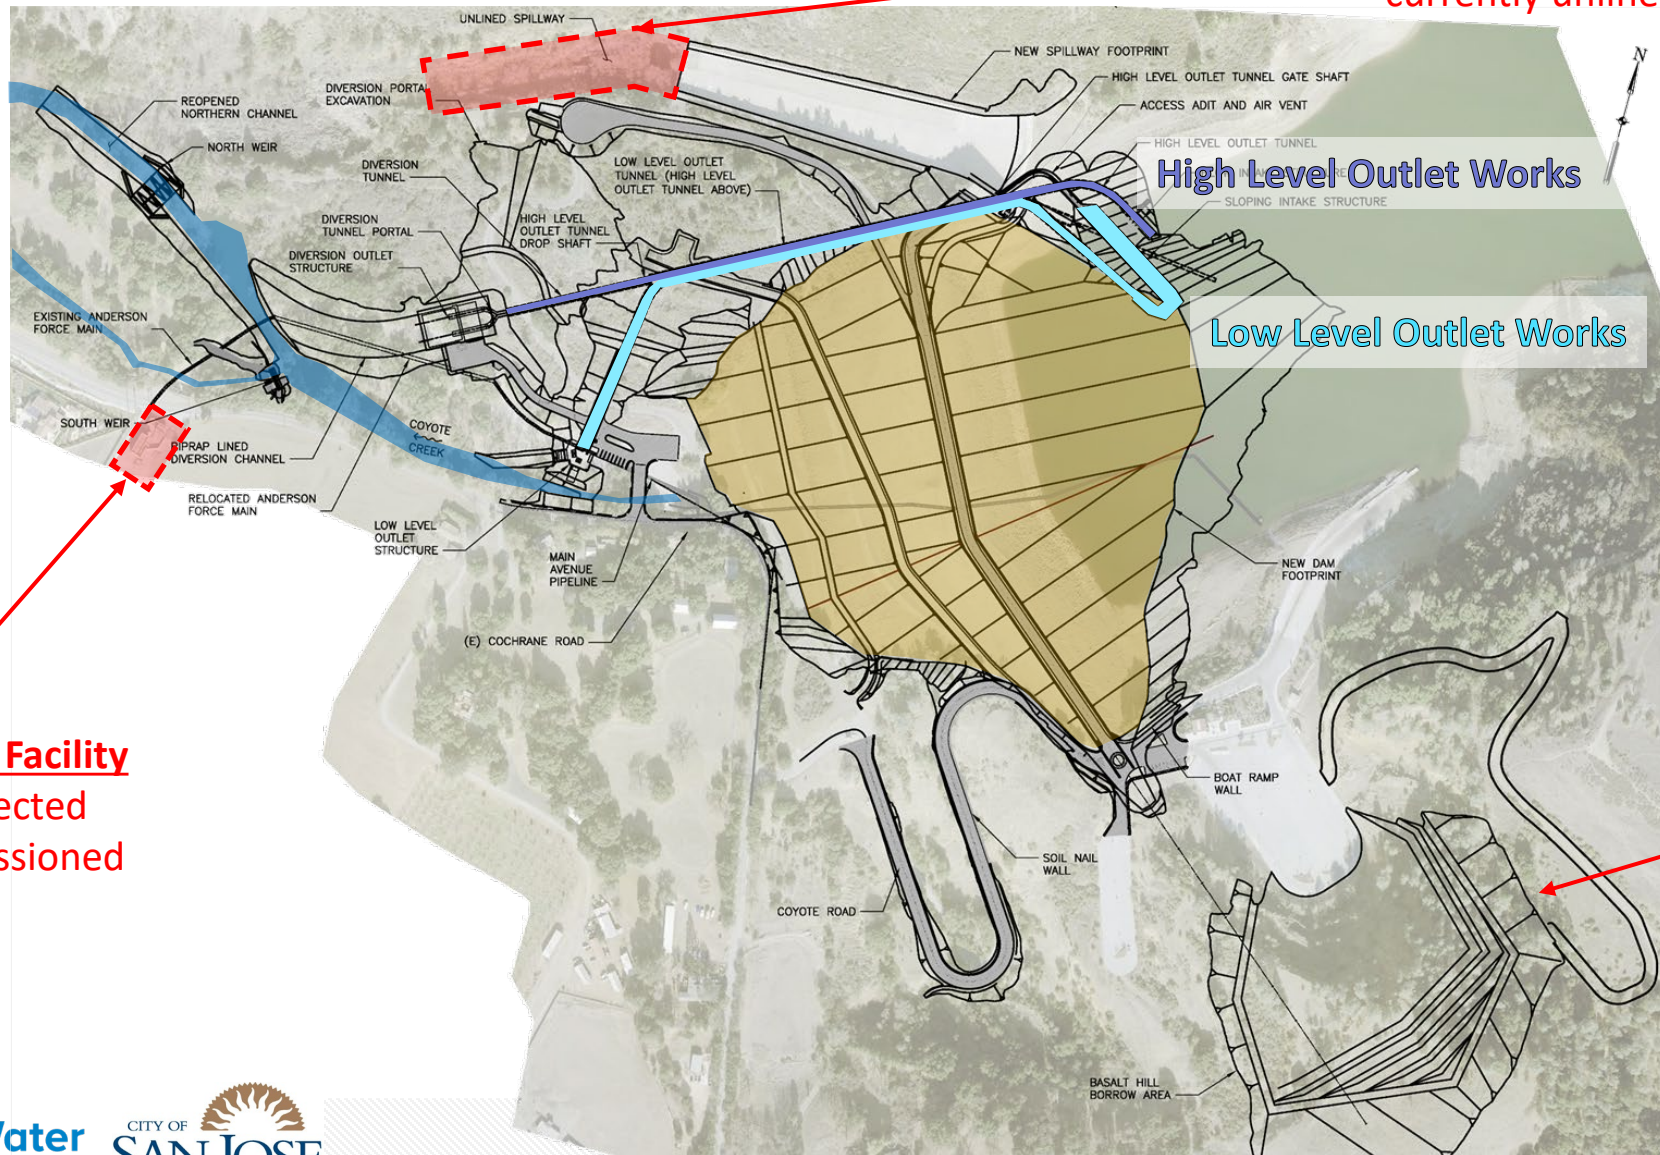

Hydroelectric Facility  
to be disconnected  
and decommissioned

Basalt Hill Borrow Area

Existing stockpile and  
future borrow area

3


valleywater.org



# Anderson Dam Tunnel Project – in construction

4


valleywater.org

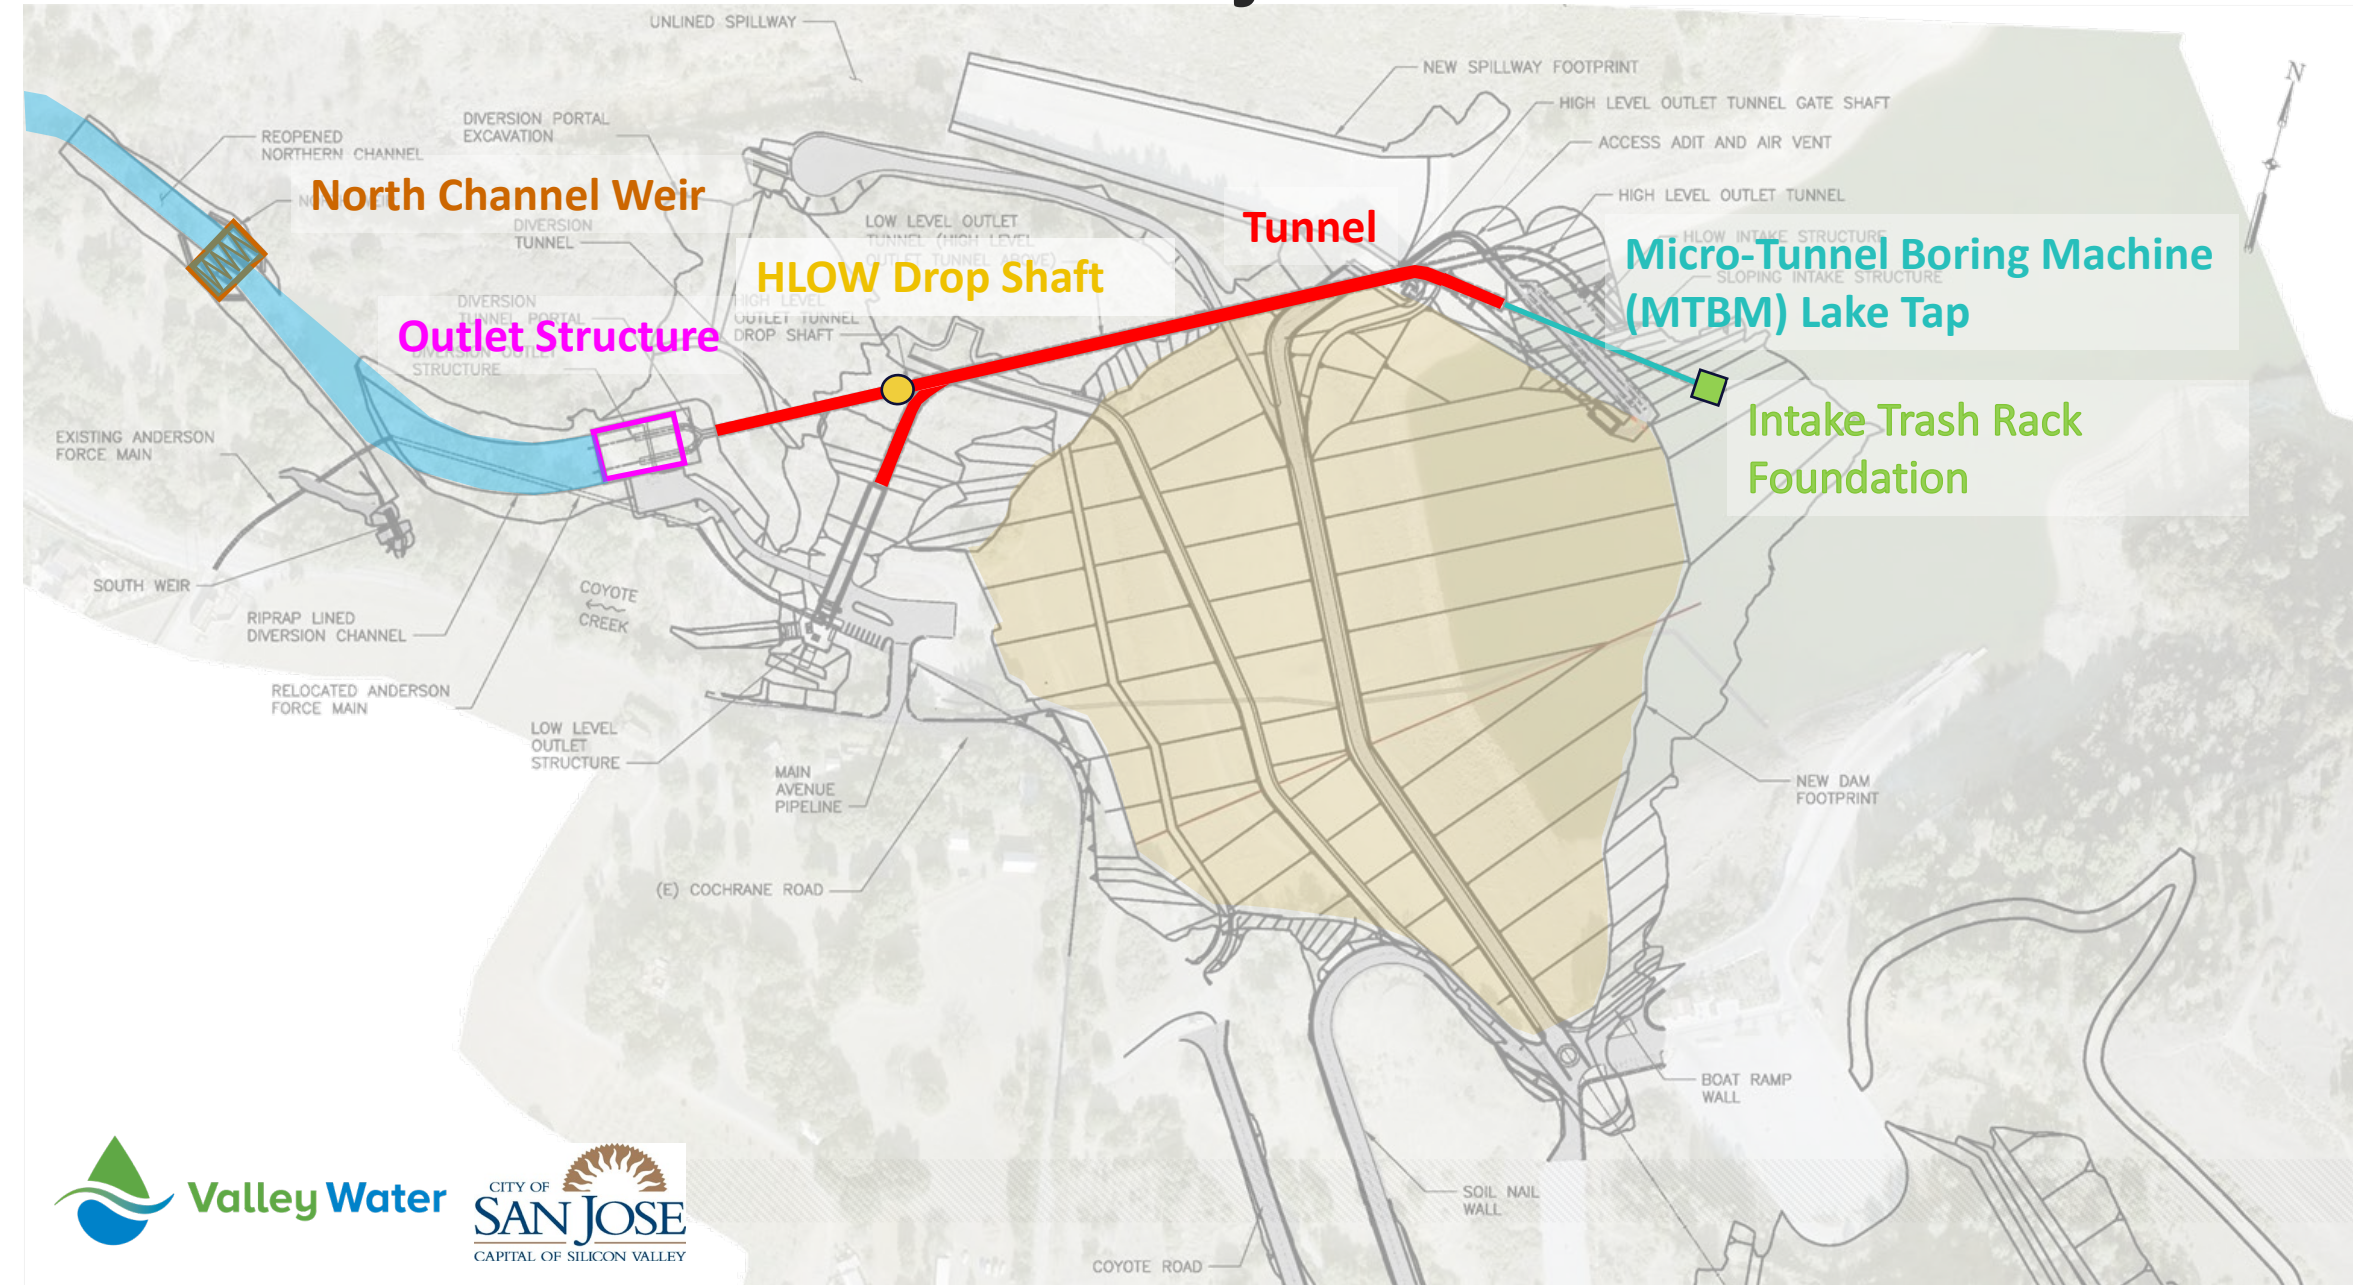



# Stage 1 Diversion – ADTP Tunnel Final Lining

5

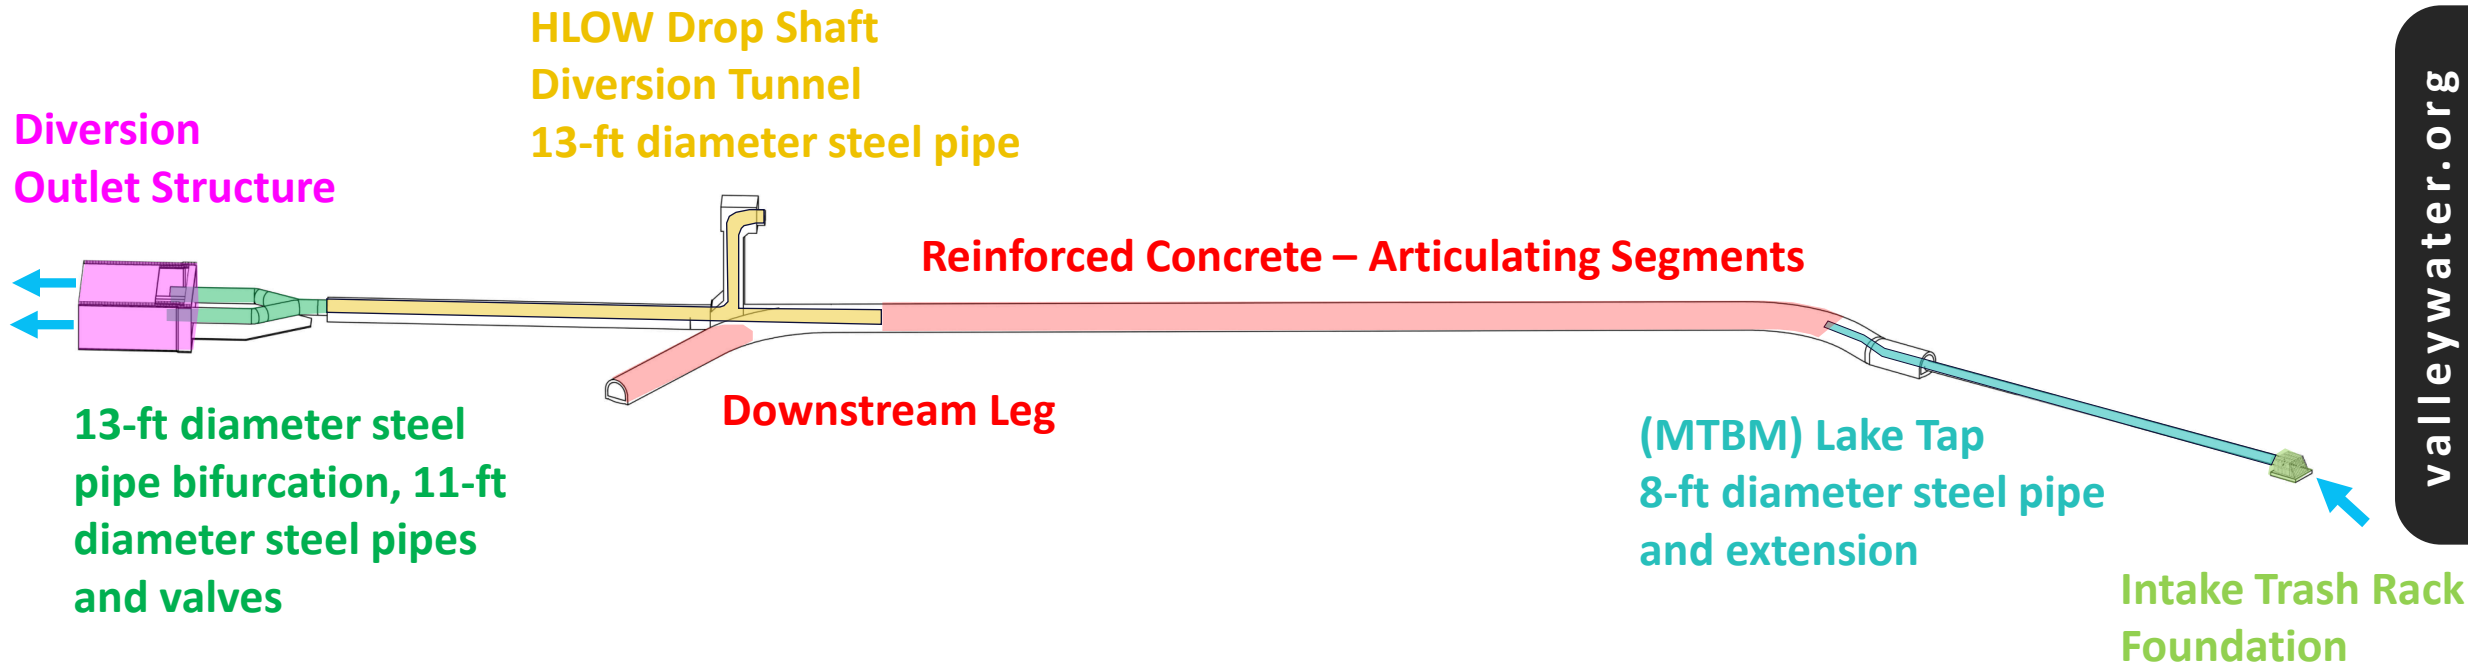



# ADTP Progress

September 2021

Beginning of site  
grading at the  
tunnel portal



November 2024

**Tunnel**  
**HLOW Drop Shaft**  
**Diversion Outlet Structure**  
**North Channel Weir**





# Structural Tunnel Lining – Articulating Segments



March 2025 – Downstream Leg  
Arch rebar complete and waterproofing in invert




July 2025 – Downstream Leg  
Invert and arch concrete placed



# Program Schedule


8

FERC Order Compliance Projects

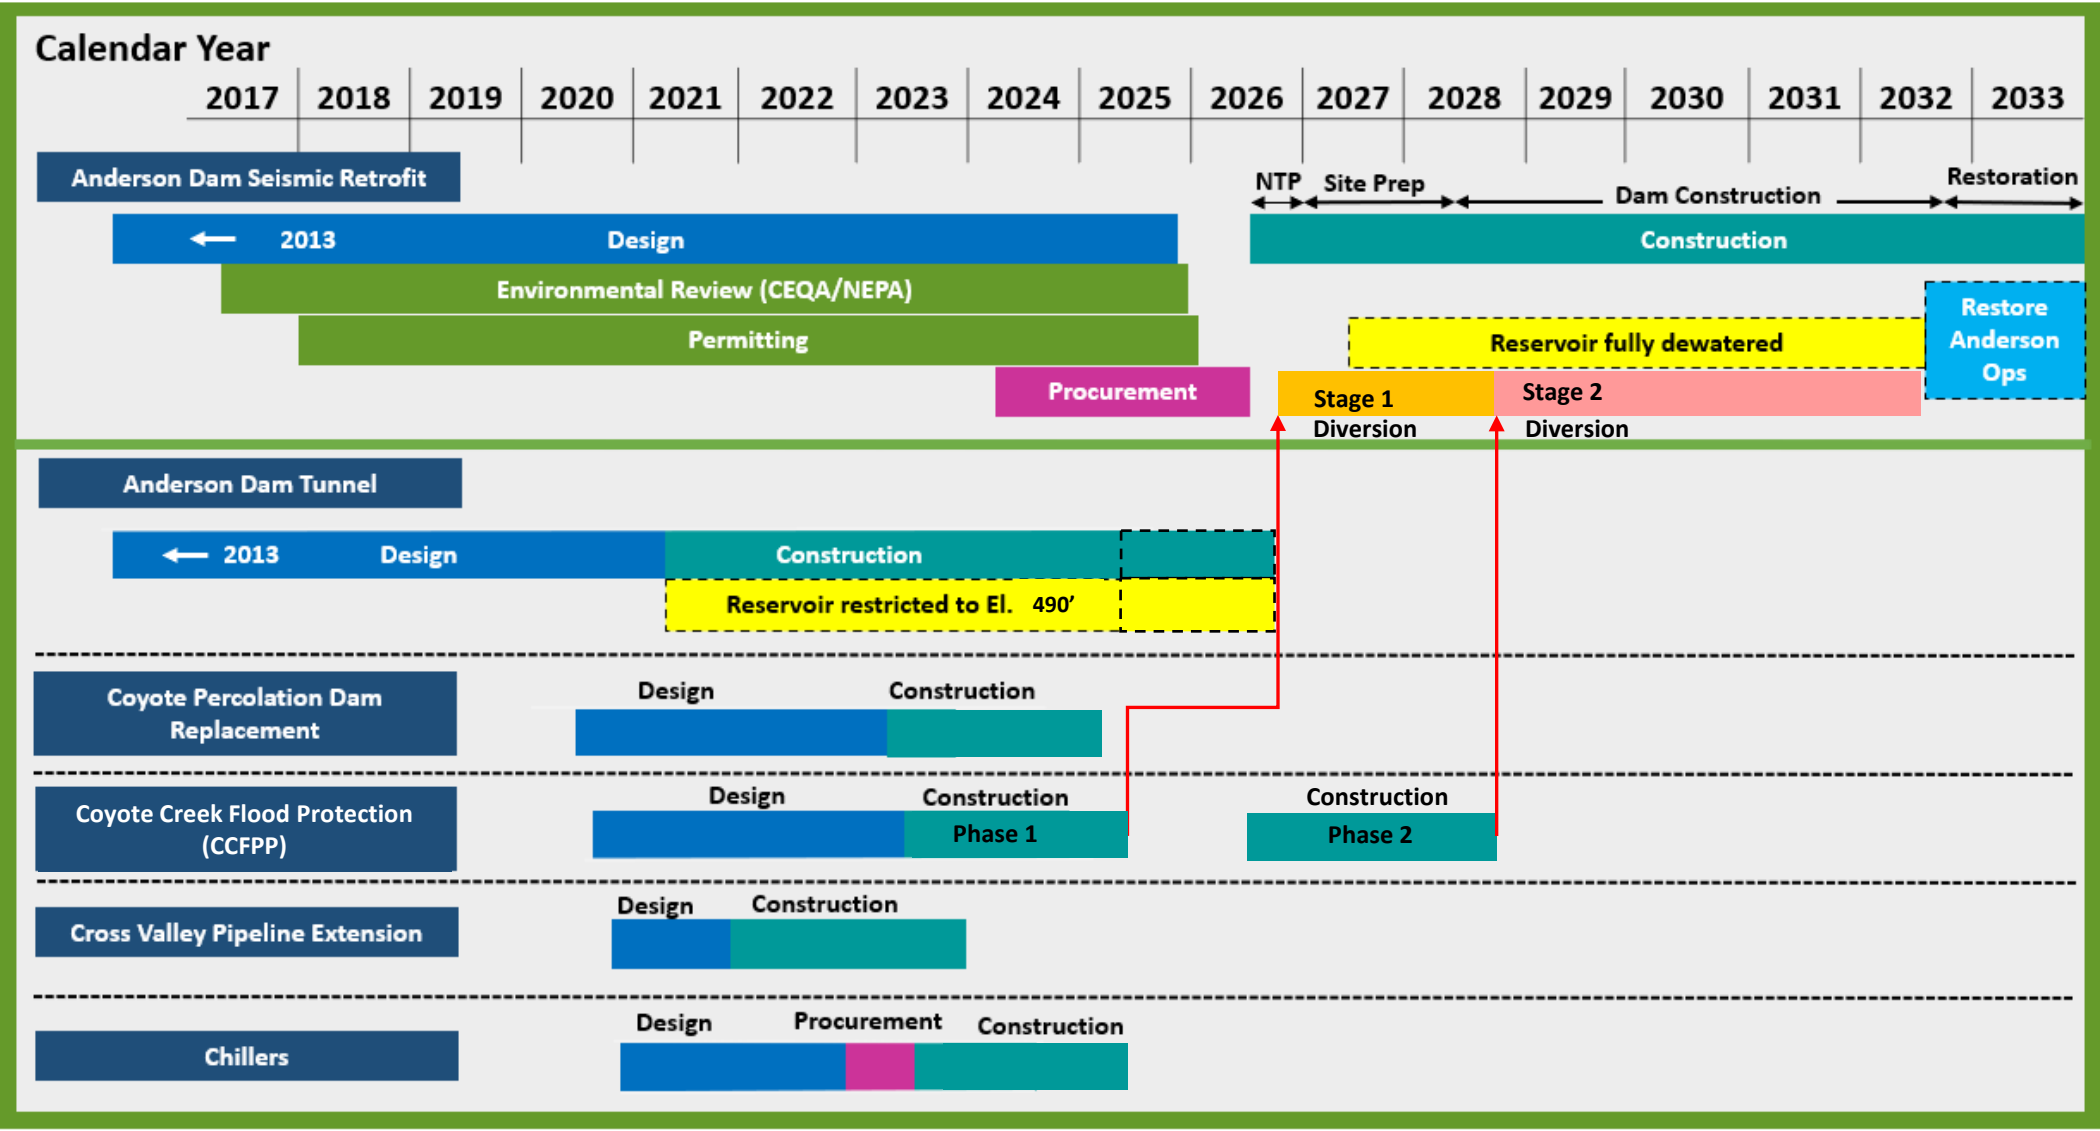

# Coyote Creek Flood Protection Project

9

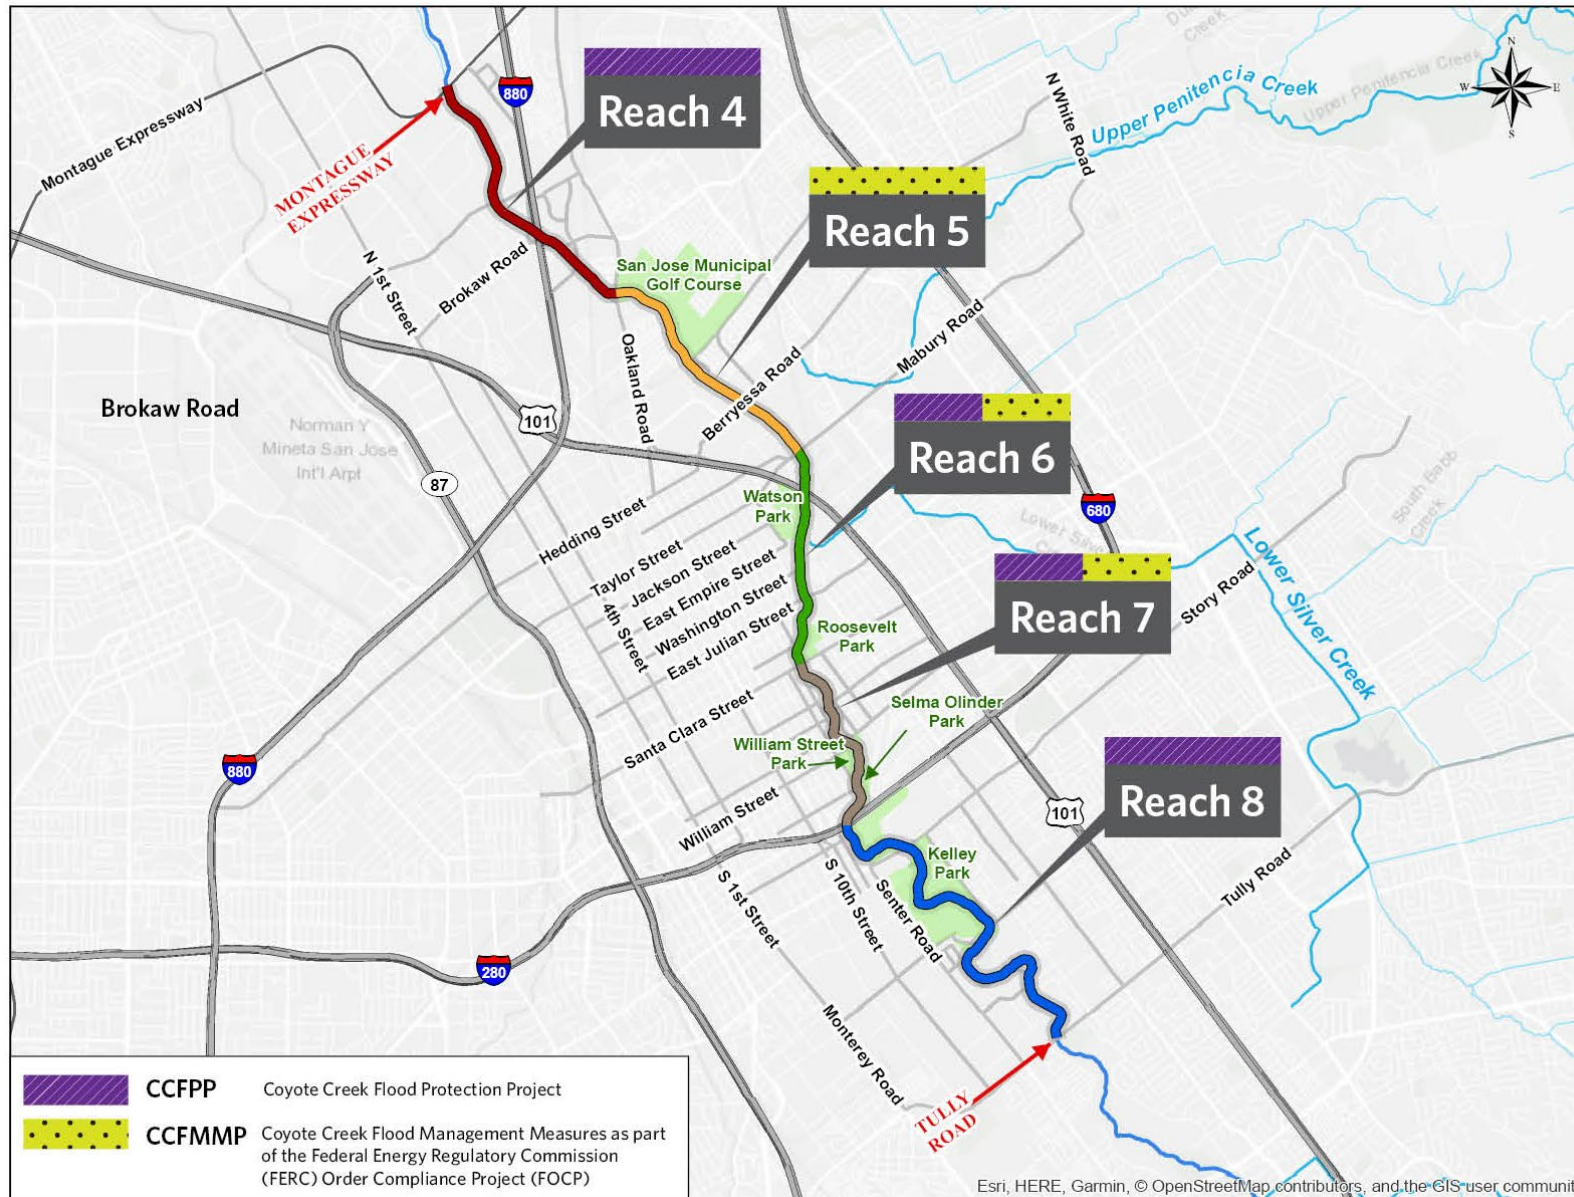


- Board awarded construction contract for CCFMMP (Phase 1) on May 16, 2023
- Board accepted the CCFMMP (Phase 1) work as complete on (June 24, 2025)
- CCFMMP (Phase 1) Project CEQA Exempt due to FERC Order
- CCFPP (Phase 2) – Board certified Final EIR on March 11, 2025
- CCFPP – Planned construction start date (Mid 2026)





# Project Schedule

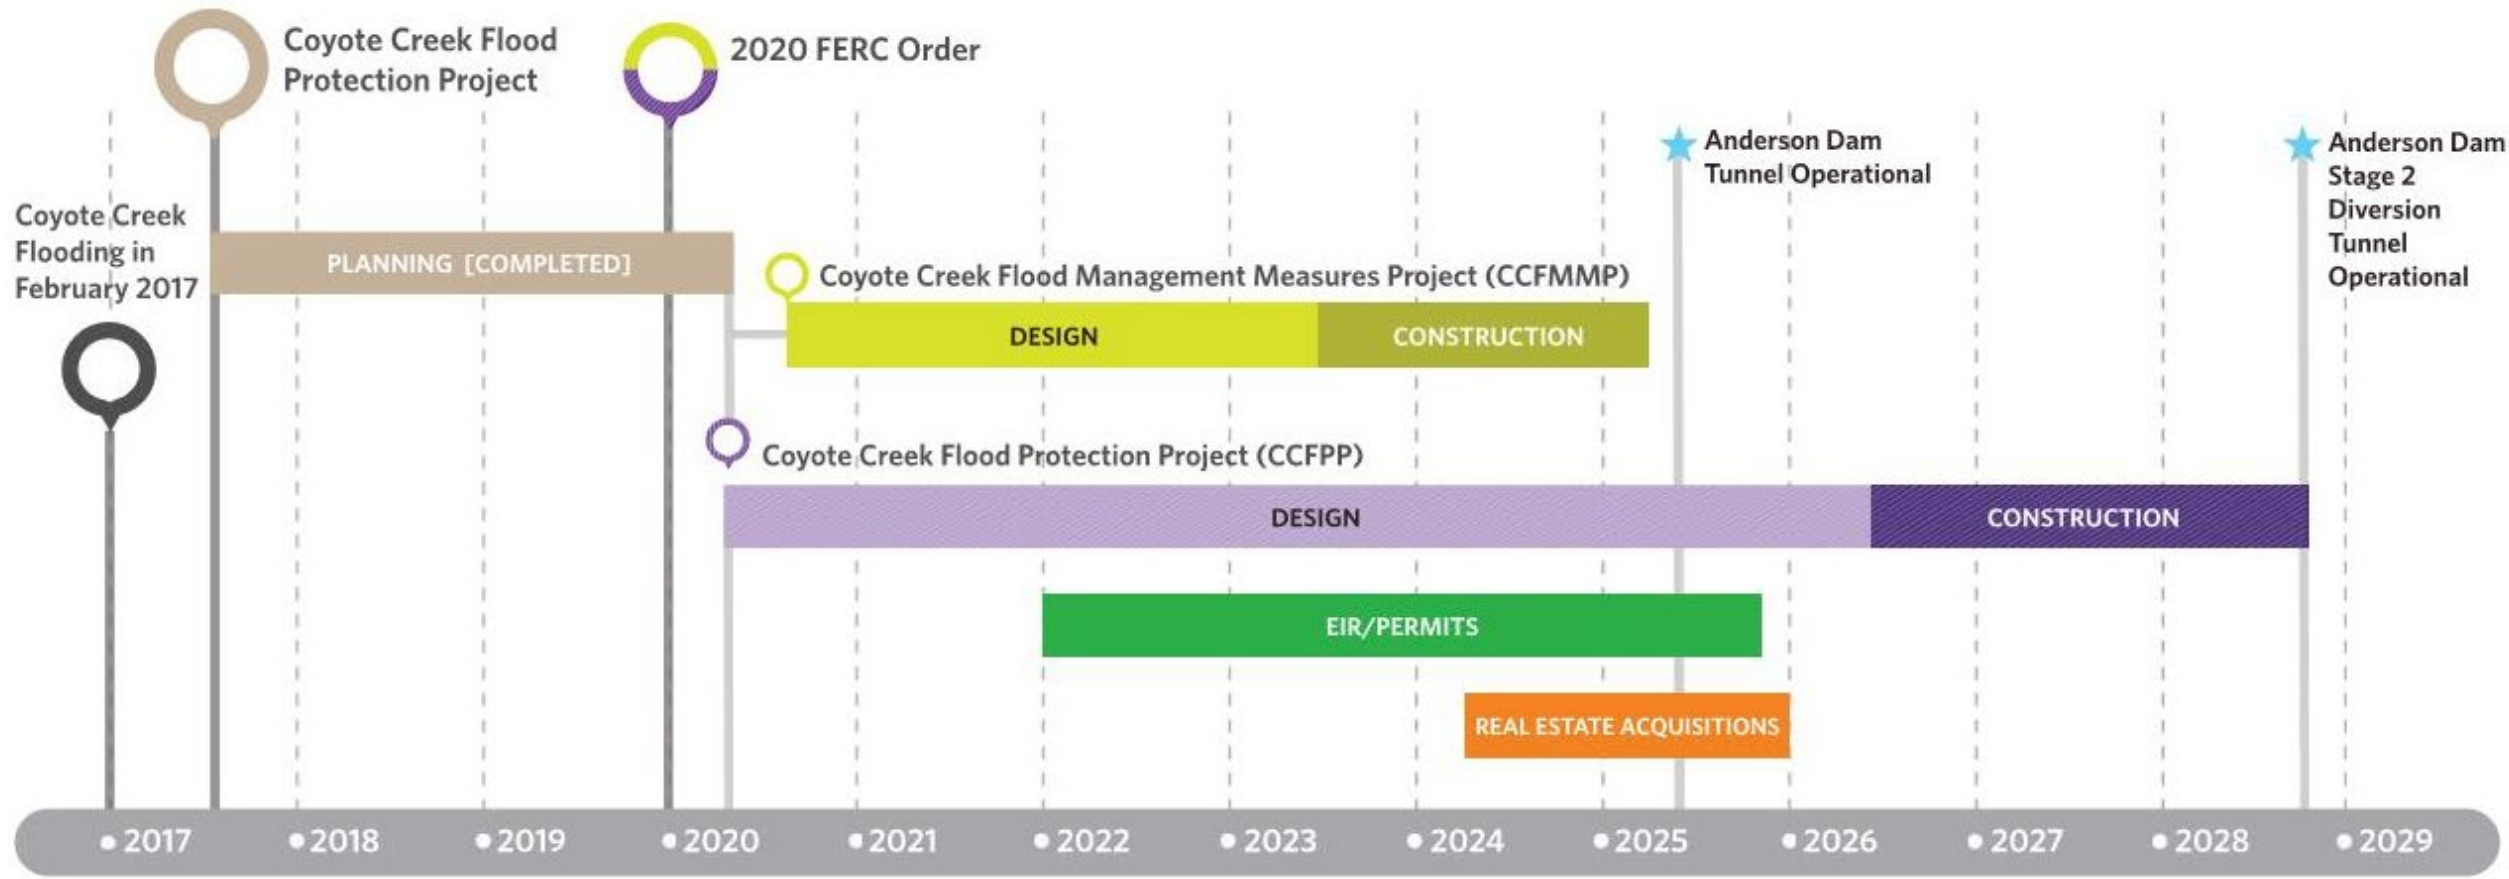



# Construction Photos




Floodwall 7



# CCFMMP Encampment Relocation – Impacted Reaches

12

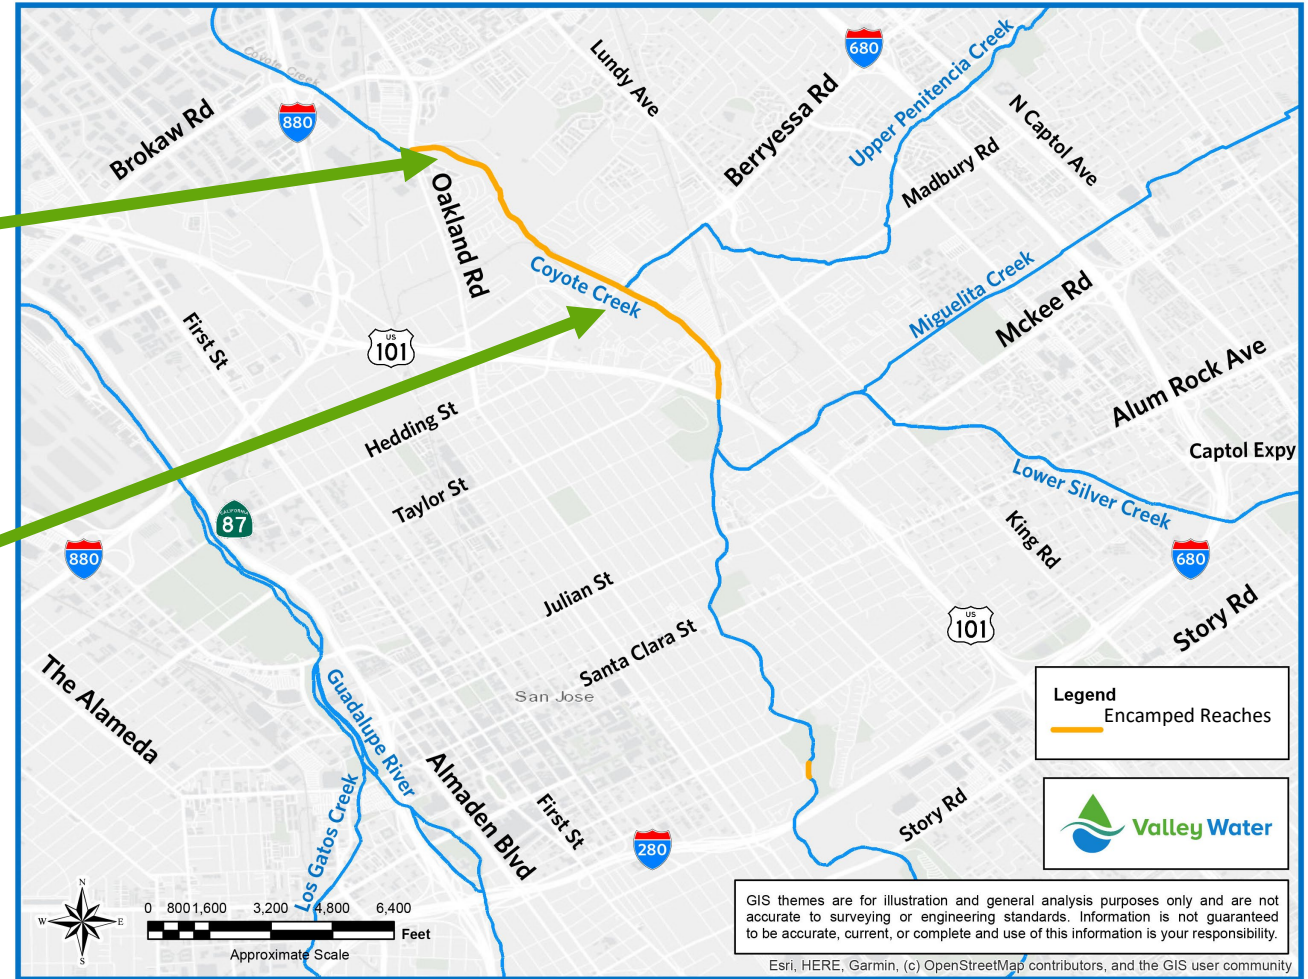

Document Name: Coyote Projects




# CCFMMP Encampment Relocation – Before & After





# CCFMMP Encampment Relocation – Outcomes

14




- Individuals with no identifying information
- Individuals who did not utilize any shelter or interim housing
- Total number of individuals placed at Guadalupe EIH (since May 2023)
- Individuals exited to shelter or other interim housing (enrolled or not)

178 total individuals provided outreach services during agreement term



# City of San José No Encampment Zones

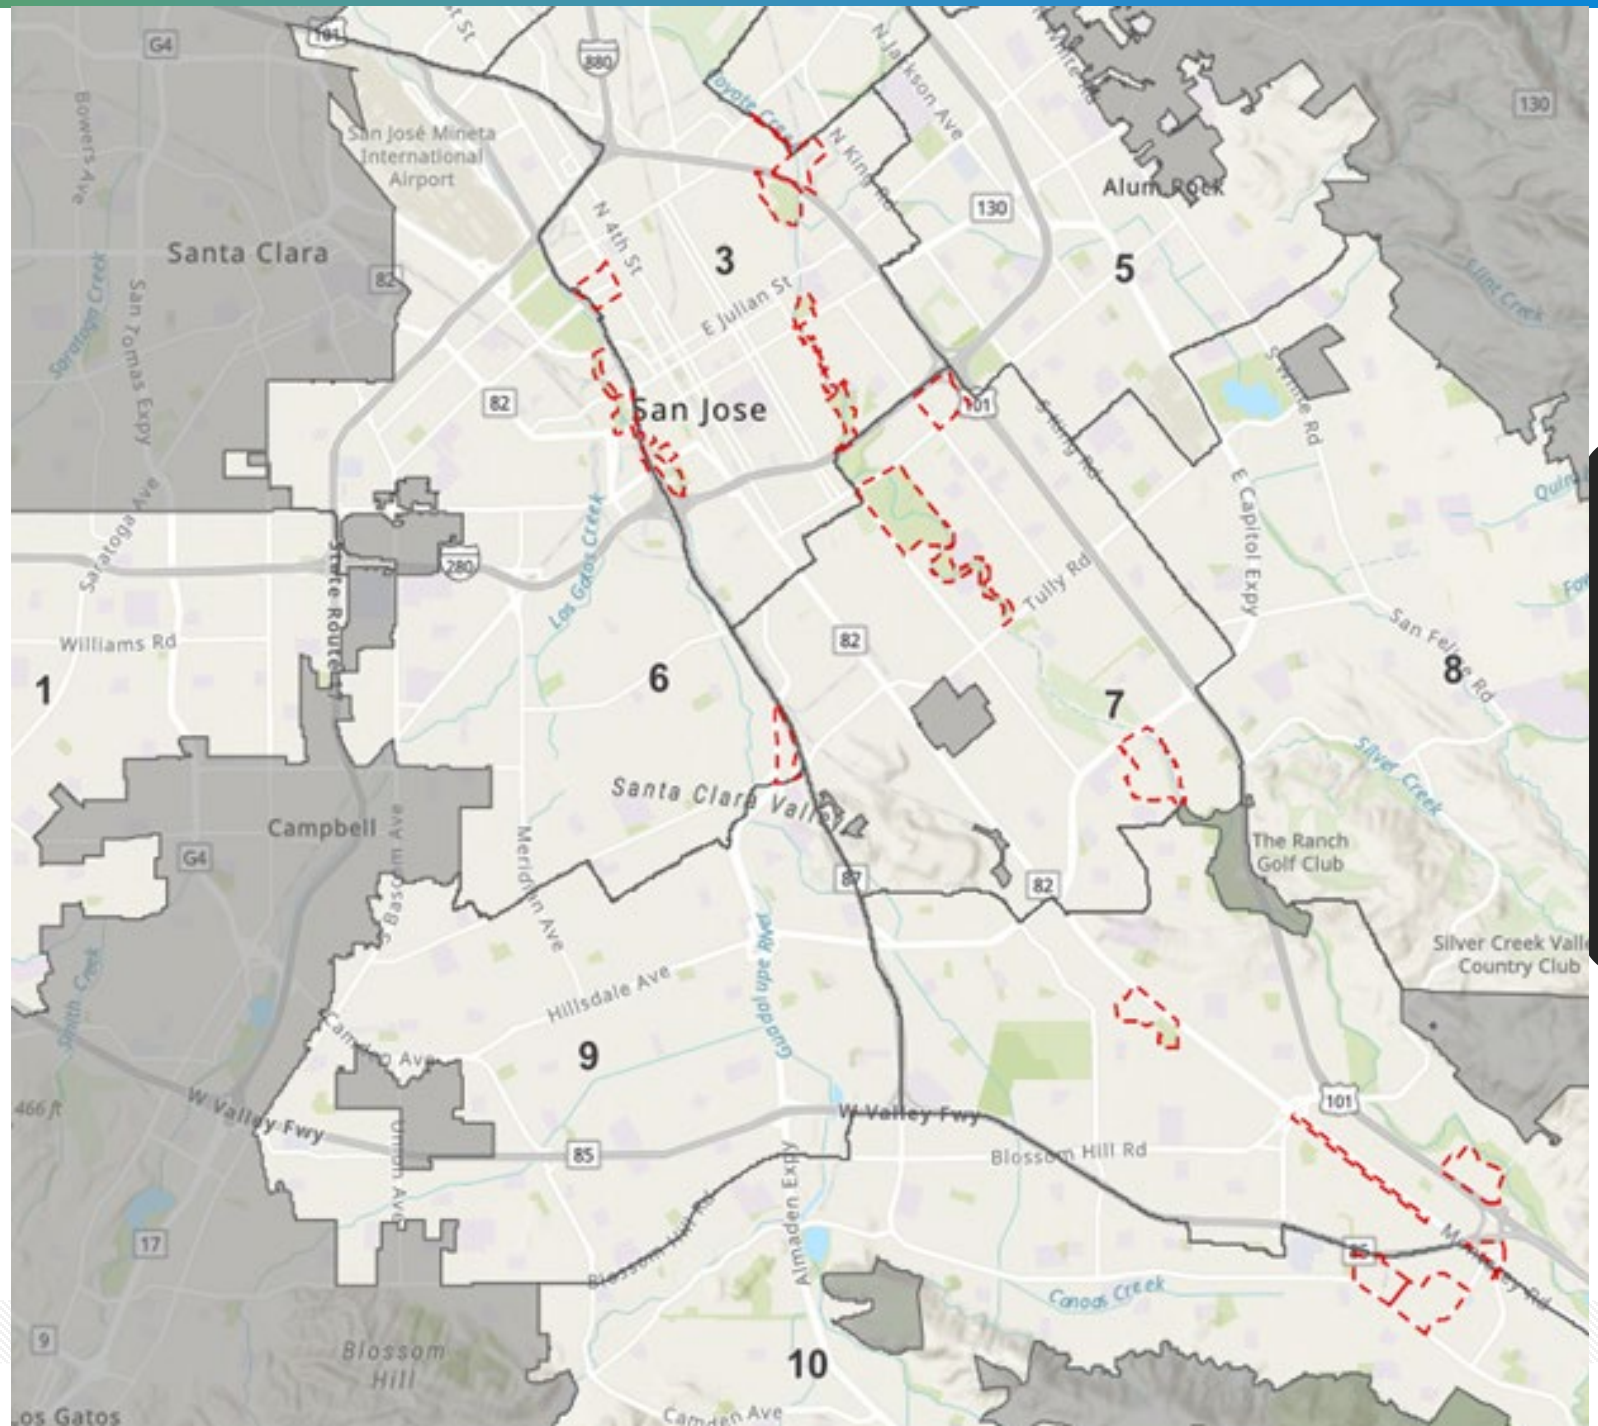



# Questions?

