

PUBLIC SAFETY COMMUNICATIONS INTEROPERABILITY SEMI-ANNUAL REPORT


Public Safety, Finance, and Strategic Support Committee

May 17, 2018

Item: (d) 1



SVRCS Sites

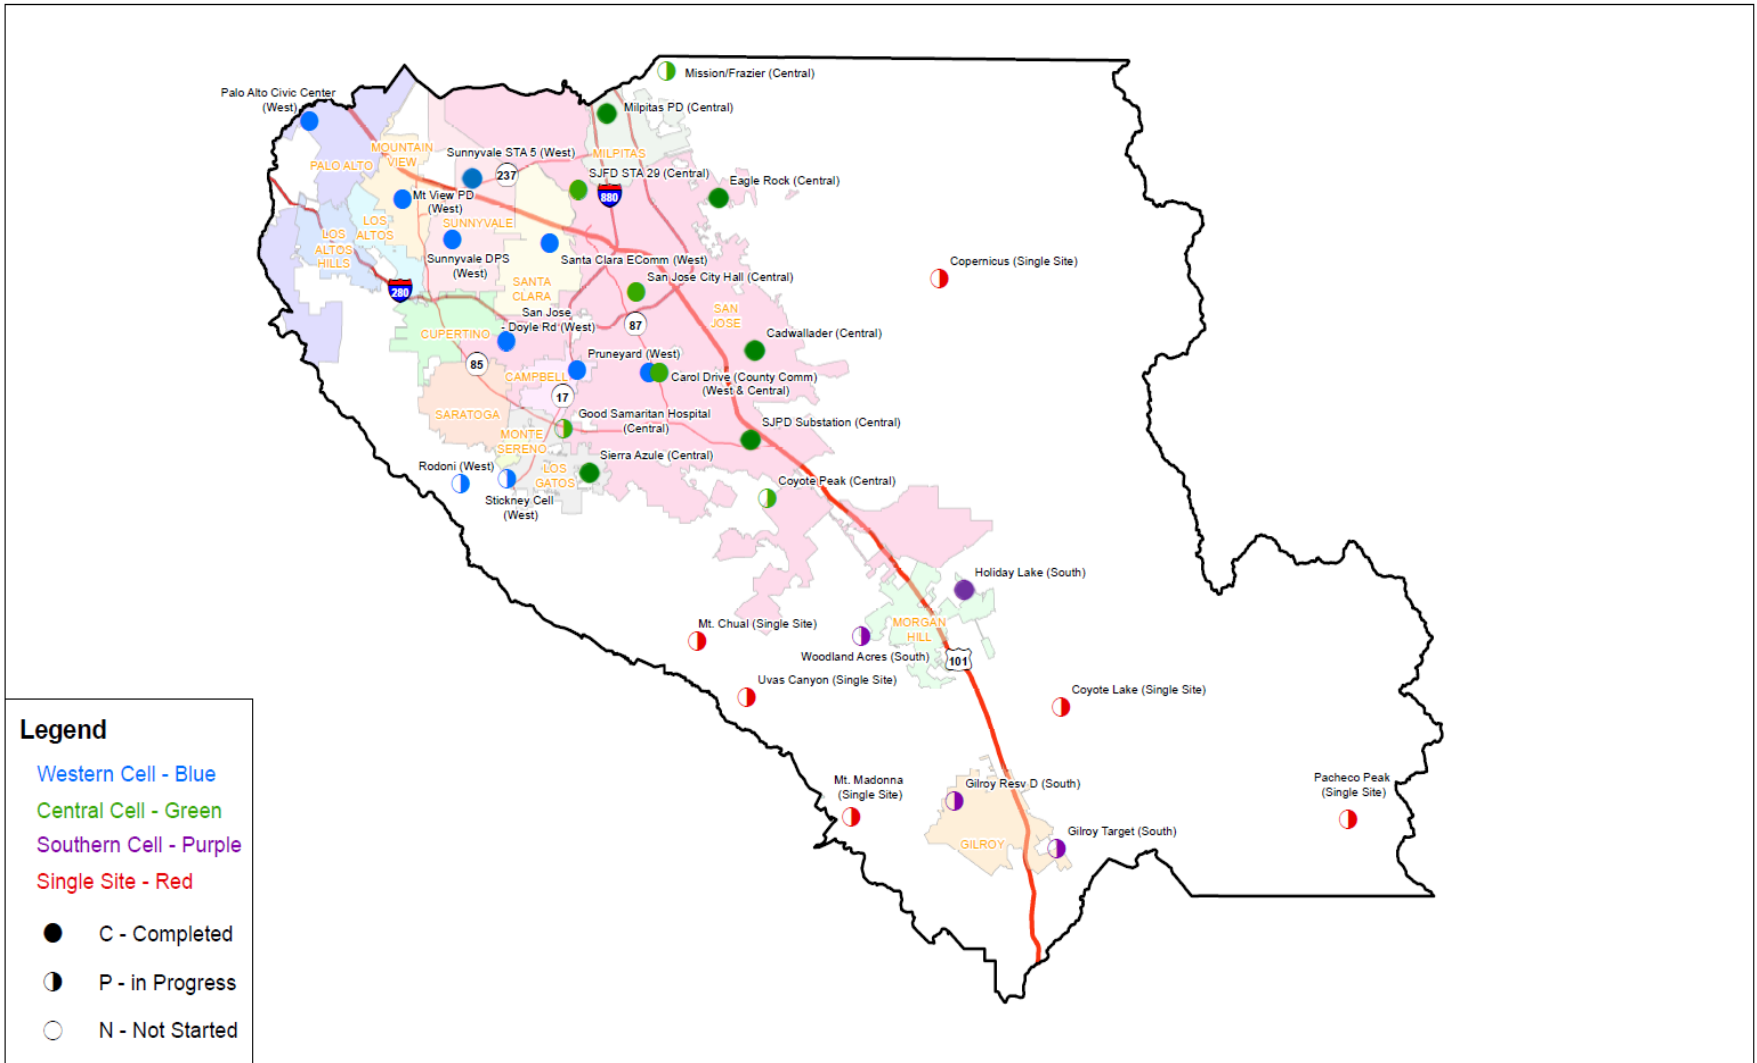

San Jose Migration Requirements

- **Central Cell Infrastructure (Covers SJ)**

December 2017 – 8 of 11 operational

Good Samaritan Hospital and Frazier 30 to 45 days away from activation

Q3 of 2018 – all 11 sites estimated to be completed

- **Authorized Radios for San Jose = 2,750**

(Police, Fire, DOT, PBCE, ACS, PRNS, and ESD)

Purchased to date: 2,330

Current Radios needed to go live: 2,748

Total of 615 additional radios

(\$2.35 million / \$750K funded in FY 18/19).

- **Dispatch Consoles for Police & Fire (Funded)**

14 for Alternate PSAP (Installed)

33 for PSAP (Installation in progress)



FirstNet Update

- March 30, 2017 AT&T selected by FirstNet
- CalOES negotiated improvements to the California Plan
- California Opted in December 28, 2017
- AT&T providing access to existing commercial 4G LTE with priority and preemption.
- March 30, 2018 AT&T FirstNet Core online
- San Jose developing a testing plan for current 4G LTE offering



Upcoming Meetings

SVRIA Board of Directors Meetings

May 24, 2018

July 26, 2018

September 27, 2018

SVRIA Working Committee Meetings

July 9, 2018

September 10, 2018

BayRICS Board of Directors

July 12, 2018

October 11, 2018

