

Public Safety Communications Interoperability Report


Public Safety, Finance, and
Strategic Support Committee

December 13, 2018

Item: (d) 2



SVRCS Sites

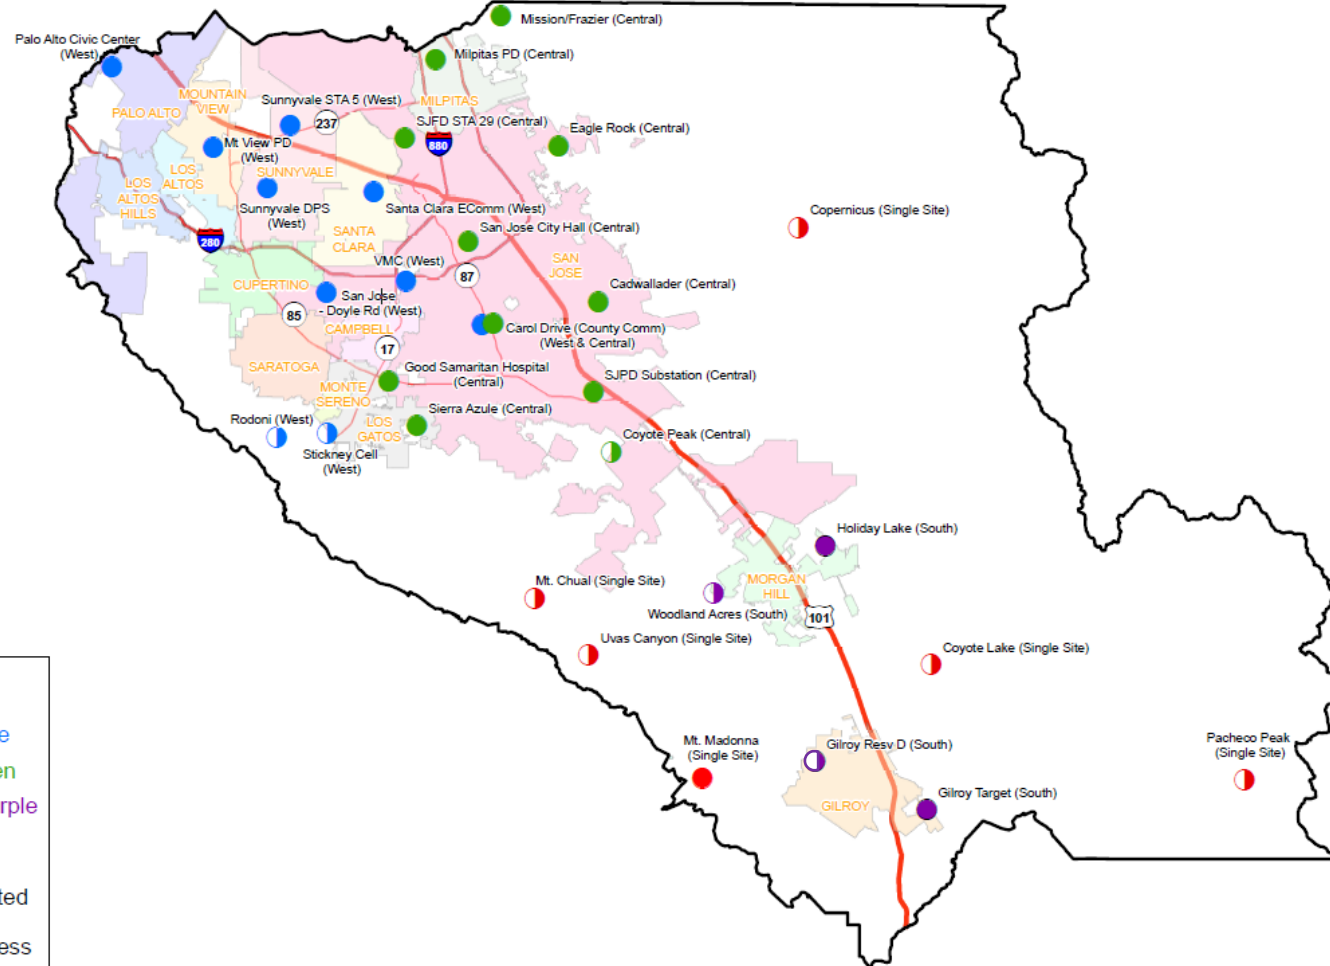

Legend

Western Cell - Blue
Central Cell - Green
Southern Cell - Purple
Single Site - Red

● C - Completed
◐ P - in Progress
○ N - Not Started



San Jose Migration Requirements

- Central Cell Infrastructure (Covers San Jose)
 - As of Dec 2018, 10 of 11 are operational
 - Coyote Peak estimated completion date: 7/24/19
- Authorized Radios for San Jose = 2,750
 - For Police, Fire, DOT, PBCE, ACS, PRNS, and ESD
 - Purchased to date: 2706
 - Current Radios needed to go live: 2868
 - Radios Remaining to be Purchased: 329
 - Outstanding radios have been budgeted through the 2021-2022 Communications Capital Improvement Program, General Fund, and through various grant opportunities.
- Dispatch Consoles for Police & Fire (Installed)
 - 14 for Alternate PSAP
 - 33 for PSAP



FirstNet Update

- March 30, 2017, AT&T selected by FirstNet
- CalOES negotiated improvements to the California Plan
- December 28, 2017, California Opted in
- March 30, 2018, AT&T FirstNet Core online
- FirstNet spectrum, Band 14, being built out
- San Jose testing current 4G LTE offering and existing Band 14 capabilities in upcoming events



Upcoming Meetings

SVRIA Board of Directors Meetings

January 24, 2018

March 28, 2019

SVRIA Working Committee Meetings

January 14, 2018

March 11, 2019

BayRICS Board of Directors

January 10, 2019

